

## SAINT MICHAEL AND ALL ANGELS CONSTRUCTION HIGHLIGHTS



### PROJECT TEAM

THE BECK GROUP – PROJECT LEADER  
Graham Comstock  
PRITCHARD ASSOCIATES - Representative  
Brett Ratliff  
SAINT MICHAEL AND ALL ANGELS  
Colleen O’Hara




### First Two Weeks of October:

- Demolition continues
- Phase 2 logistics are completed
- Demolition of existing buildings wraps up
- Demolition of existing foundation is completed
- Many materials are recycled such as steel concrete, copper, etc.

### Last Two Weeks of October:

- Continue to make progress on Phase 2
- Demolition is completed on Phase 2
- Earthwork begins on Phase 2
- 80 truck loads removed each day
- Dirt is stockpiled on site for future backfill
- Piers began at the expanded ambulatory

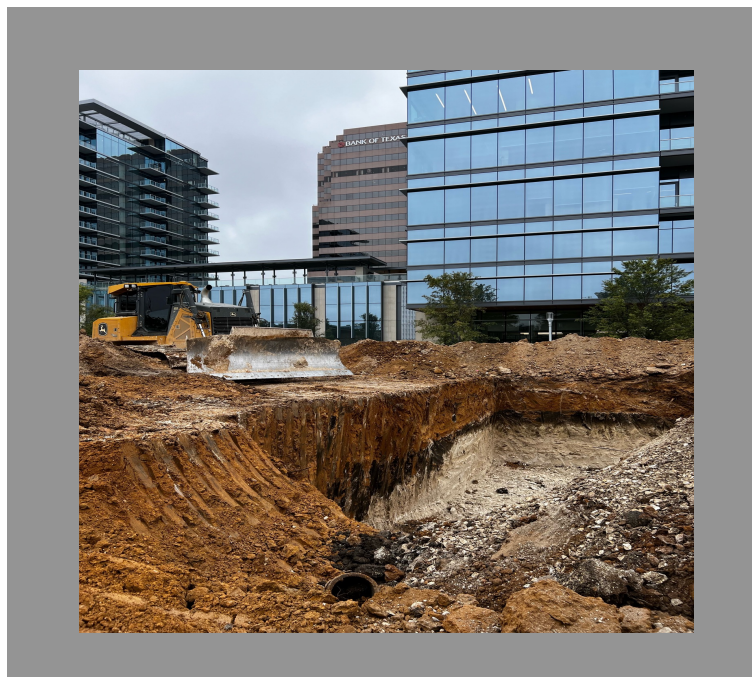

### Looking Forward...

As we move into November, we will progress on the below grade portion of Phase 2:

- Completing basement excavation
- Drilling piers
- Completing grade beams
- Preparing for the tower crane
